


Pre-Inspection Checklist	
<b>Project:</b> Taylor Wimpey North Finchley site	<b>Date:</b> 26 October 2024
<b>Area:</b> Block D	<b>Am / Pm:</b> AM
<b>Locaton:</b> Block D	<b>Drawing Number:</b> 22227-RAS-D-FN-GA-S-00002 C02
<b>Weather Condition:</b> Dry	<b>Sheet Number:</b> 1

Table of Contents

- Setting Out Line & Level to Current Drawings
- Correct Formation Depth Achieved
- Concrete Blinding to Depth Specified
- Rebar to Specified Drawing
- Concrete Specification
- Concrete Specification for Finish
- Post Pour Level Check

Completed By: LP

Date Completed: 26 October 2024

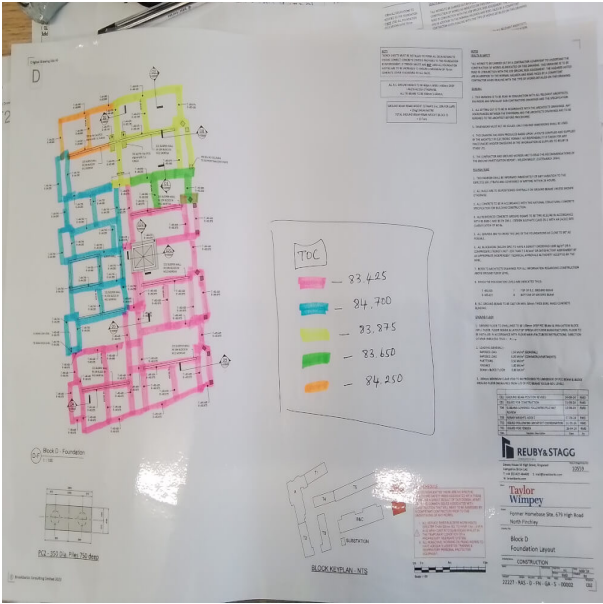



**Completed By:** LP


**Date Completed:** 26 October 2024



**Completed By:** LP

**Date Completed:** 26 October 2024

**(a) material POLYPIPE**

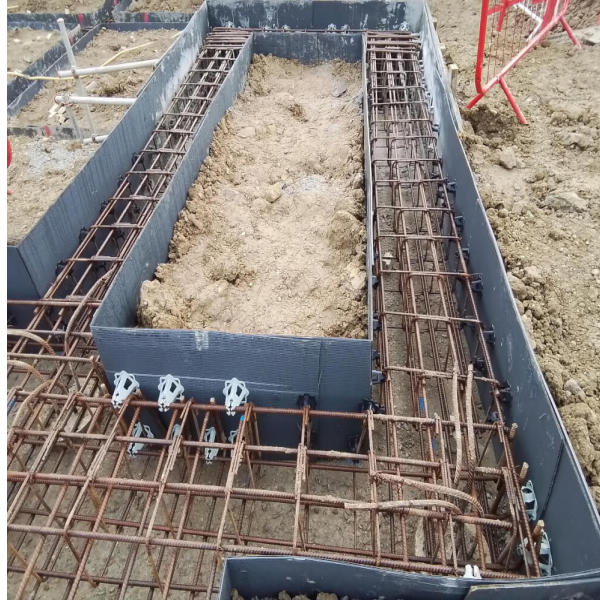



Completed By: LP


Date Completed: 26 October 2024





Completed By: LP

Date Completed: 26 October 2024

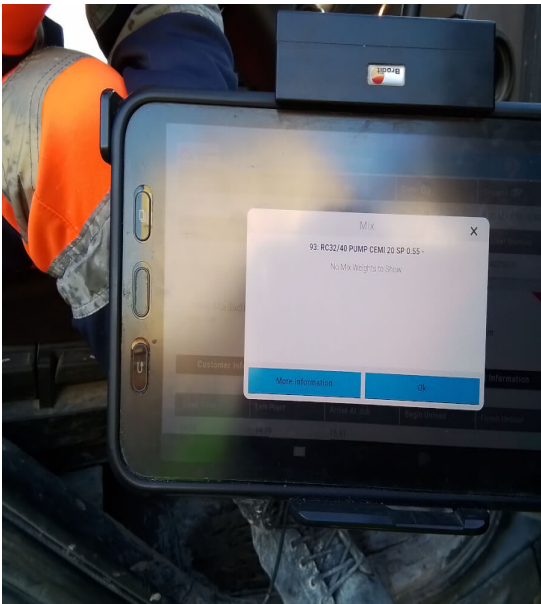

Completed By: LP

Date Completed: 26 October 2024





Completed By: LP

Date Completed: 26 October 2024

Additional Measures:





Proceed/not proceed

Reason for Rejection/Comments: Integrity testing for piles has been completed by Franki piling contractor Pile cut has been inspected by NHBC inspector Pre pour inspection has been passed by NHBC inspector and Taylor Wimpey Site manager and Authorised to cast ground beams for block D Additional ground beams and pilecaps poured on 25.11.2024 due to design changed

Signed for HOULIHAN: Logesparan Priyaparan

Date: 2024-10-26

Signed for client by: Harvey scott

Date: 2025-03-28

The above inspections have been carried out and are acceptable/unacceptable

Non Conformities/Comments

Reason for non Conformities/Comments: na

Signed for HOULIHAN: Logesparan Priyaparan

Date: 2025-03-04

Signed for client by: Harvey scott

Date: 2025-03-28
