

Pre-Inspection Checklist	
Project: Taylor Wimpey North Finchley Site	Date: 13 May 2025
Area: Block T1	Am / Pm: AM
Locaton: Block T1 Ground beams	Drawing Number: 22227-RAS-T1-FN-GA-S-00002 C01
Weather Condition: Fine / mild	Sheet Number: 1

Table of Contents

- Setting Out Line & Level to Current Drawings
- Correct Formation Depth Achieved
- Concrete Blinding to Depth Specified
- Rebar to Specified Drawing
- Concrete Specification
- Concrete Specification for Finish

Completed By: LP

Date Completed: 13 May 2025



Completed By: LP

Date Completed: 13 May 2025



Completed By: LP


Date Completed: 13 May 2025

(a) material POLYPIPE



Completed By: LP

Date Completed: 13 May 2025

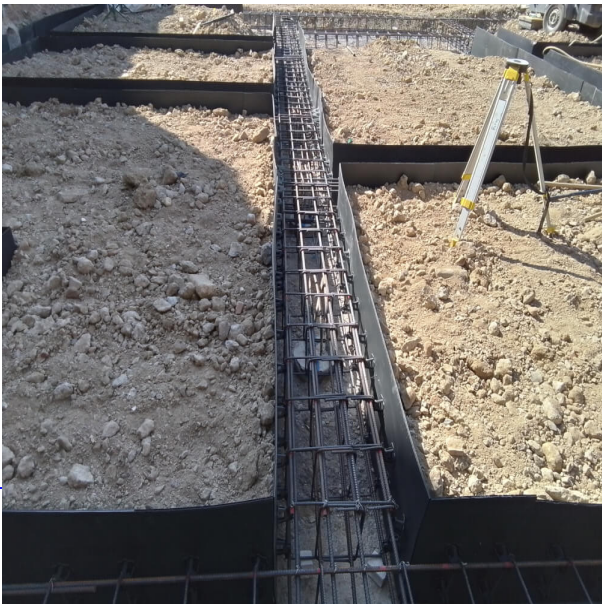

Completed By: LP

Date Completed: 21 May 2025



Completed By: LP

Date Completed: 21 May 2025



Proceed/not proceed

Reason for Rejection/Comments: Integrity testing for piles has been completed by Franki piling contractor Pilecut has been inspected by NHBC inspector Pre pour inspection has been passed by NHBC inspector and Taylor Wimpey Site manager and Authorised to cast ground beams for block T1 Franki piling contractor missing rebars for a Pile P21 and redesign and remedial work to be carried out by Franki for this section of ground beams Remedial works has been completed as per the structural engineer details and NHBC inspector inspected the work.

Signed for HOULIHAN: Logesparan Priyaparan

Date: 2025-05-21

Signed for client by: Harvey scott

Date: 2025-05-21

The above inspections have been carried out and are acceptable/unacceptable

Non Conformities/Comments

Reason for non Conformities/Comments: na

Signed for HOULIHAN: Logesparan Priyaparan

Date: 2025-05-21

Signed for client by: Harvey scott

Date: 2025-05-21
