


Pre-Inspection Checklist	
Project: Taylor Wimpey North Finchley site	Date: 15 November 2024
Area: Block B-C	Am / Pm: AM
Locaton: Block B-C	Drawing Number: 22227-RAS-BC-FN-GA-S-00002
Weather Condition: Dry / Mild	Sheet Number: 1

Table of Contents



- Setting Out Line & Level to Current Drawings
- Correct Formation Depth Achieved
- Concrete Blinding to Depth Specified
- Rebar to Specified Drawing
- Concrete Specification
- Concrete Specification for Finish
- Post Pour Level Check

Completed By: LP

Date Completed: 15 November 2024

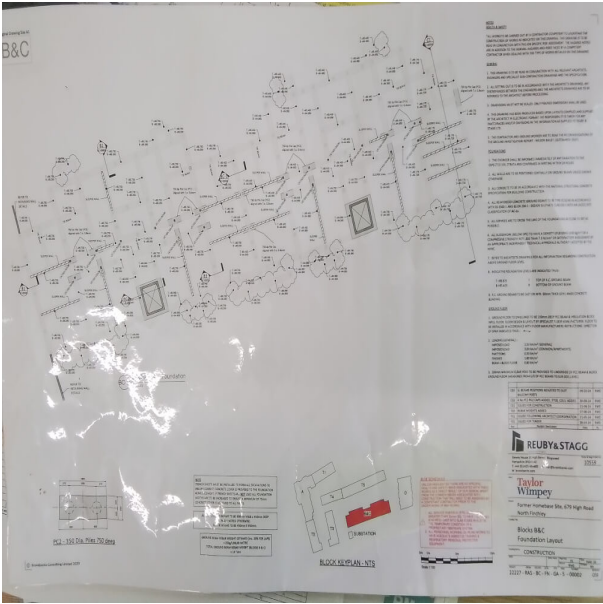

Completed By: LP
Date Completed: 15 November 2024

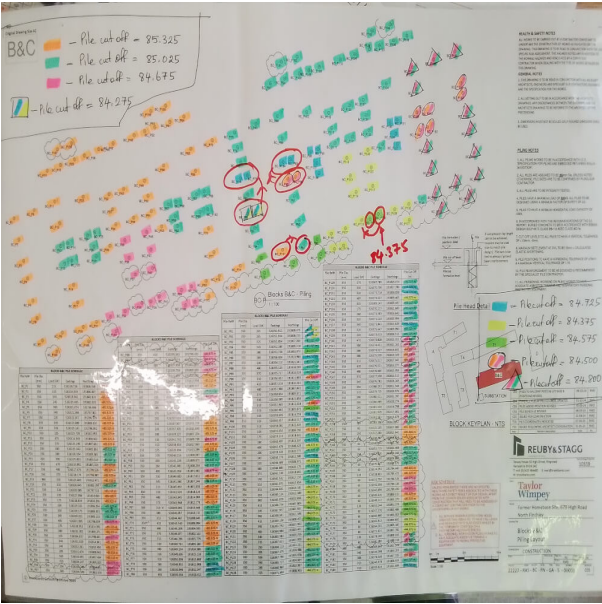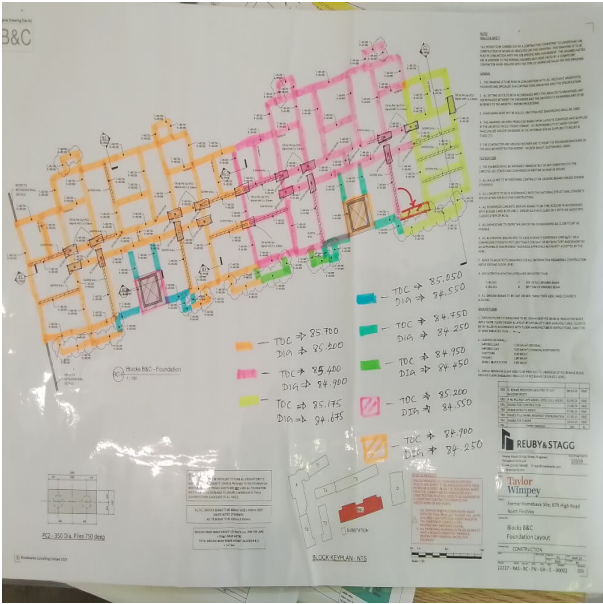

Completed By: LP

Date Completed: 15 November 2024

(a) material POLYPIPE




Date Completed: 15 November 2024



Completed By: LP

Date Completed: 01 January 1970

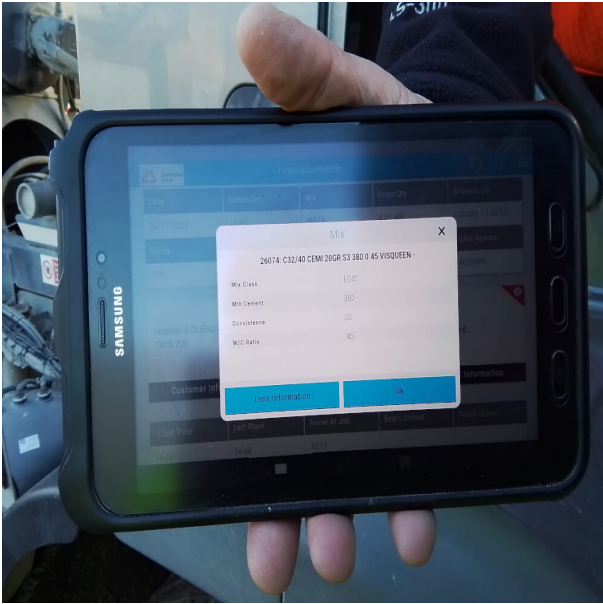

Completed By: LP

Date Completed: 01 January 1970



Completed By: LP

Date Completed: 01 January 1970

Additional Measures:



Proceed/not proceed

Reason for Rejection/Comments: Integrity testing for piles has been completed by Franki piling contractor Pile cut has been inspected by NHBC inspector Pre pour inspection has been passed by NHBC inspector and Taylor Wimpey Site manager and Authorised to cast ground beams for block B-C 2x lift base and lift wall poured with C40 visqueen waterproof admixture, VX25 waterbar installed as per the drawing and details Installed Concrete encasement for steel column as per engineer details

Signed for HOULIHAN: Logesparan Priyaparan

Date: 2024-12-10

Signed for client by: Harvey scott

Date: 2025-03-28

The above inspections have been carried out and are acceptable/unacceptable

Non Conformities/Comments

Reason for non Conformities/Comments: na

Signed for HOULIHAN: Logesparan Priyaparan

Date: 2024-12-10

Signed for client by: Harvey scott

Date: 2025-03-28
