A3 See drawing "Jetfloor 150 Details" for sections and notes

Denotes approximate position of airbrick

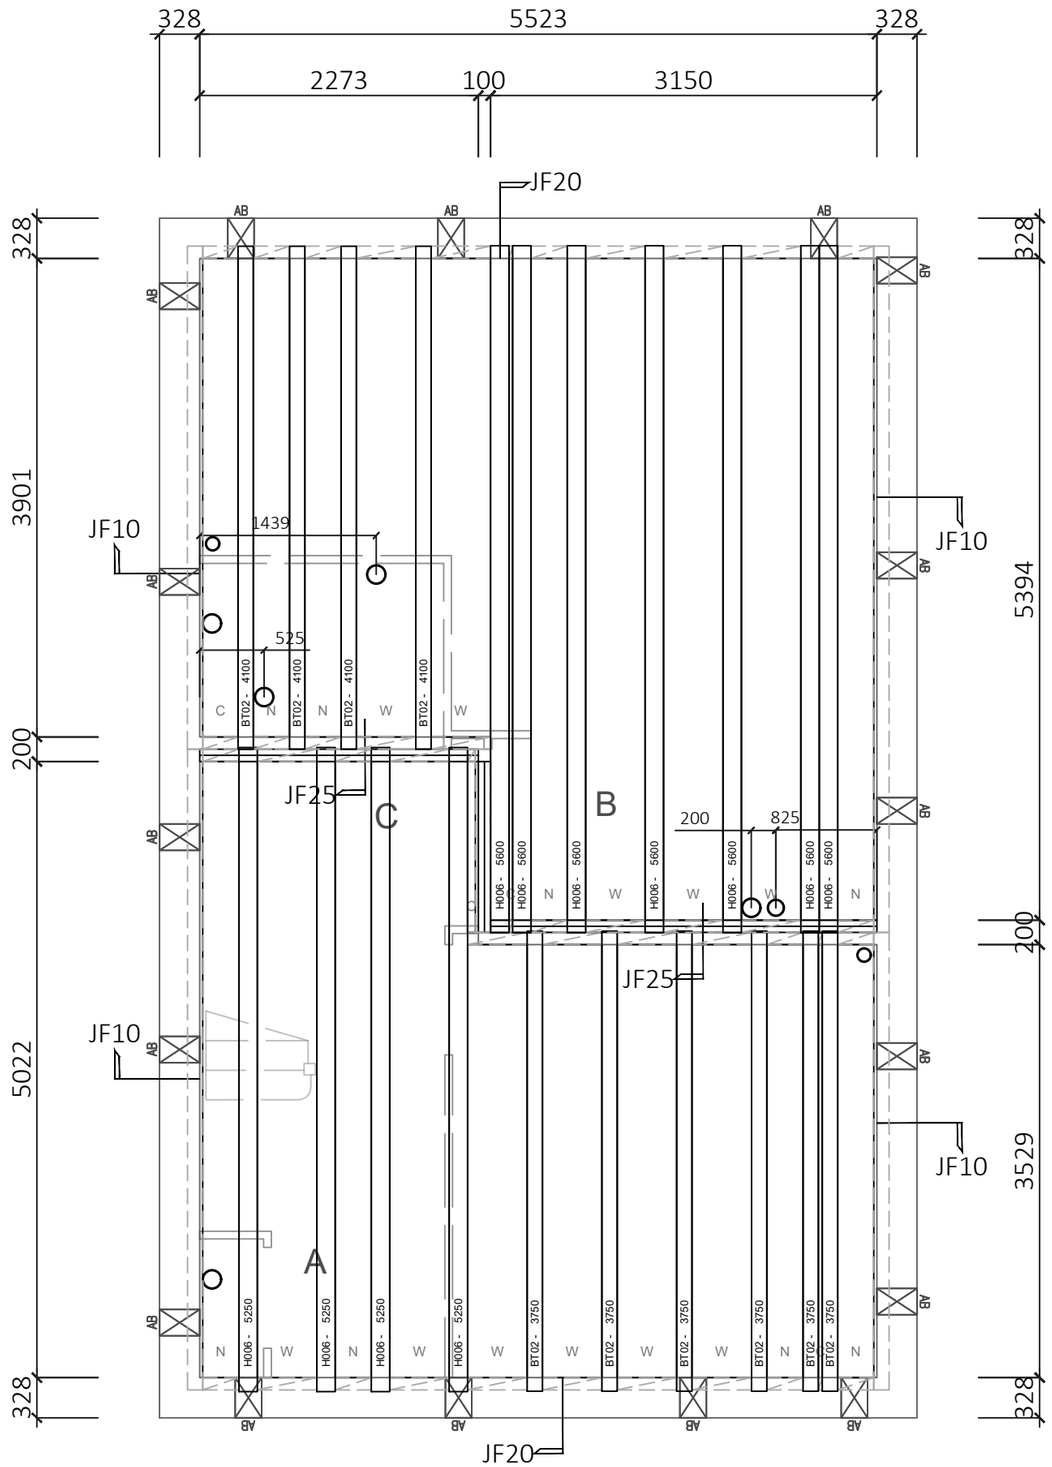

Bill of material			
NR.	ITEM		
6	BT02	BEAM	3750mm
4	BT02	BEAM	4100mm
4	H006	BEAM	5250mm
7	H006	BEAM	5600mm

J100C (white EPS 18kg/m³)	0.75
JCN (white EPS 26kg/m³)	29.74
JCW (white EPS 26kg/m³)	40.12

Coursing blocks			
SCKH 20N	: N/A	BR100L 3.6N	: N/A
SCRP 10N	: N/A	BR100W 3.6N	: N/A
SCRP 20N	: N/A	BR100N 3.6N	: N/A
TS100W 7.3N	: N/A	PS100W 7.3N	: N/A
TS100N 7.3N	: N/A	PS100N 7.3N	: N/A
JL100 7.3N	: N/A	PS140W 7.3N	: N/A
TS140W 7.3N	: N/A	PS140N 7.3N	: N/A
TS140N 7.3N	: N/A	TCBL	: 36
JL140 7.3N	: N/A	PM100L	: 90
EX100L	: N/A	PM100W	: 22
EX140L	: N/A	PM100N	: 23
EX100W	: N/A	EX140W	: N/A
EX100N	: N/A	EX140N	: N/A

Total Floor weight : 3.82 tonnes
Total Floor Area : 50 m2
Total m3 poly block : 38.378 m3
Floor weight ex blocks: 3.82 tonnes
Heaviest unit : 226.05 Kg

Overlay sheets		
J150C 17.25 pc		

Ancillary items		
Airbrick Timloc	: 17	P34 : 25 pc
Airbrick Manthorpe	: N/A	
BC1100	: N/A	
BC1140	: N/A	
BC3100	: N/A	
BC3140	: N/A	

Revisions

SFX	DATE	Comment	Initial
A	15-04-2026	Airbrick updated.	NS

Loading Allowances

Live Load	1.50	kN/m²
Dead Load	1.80	kN/m²
Blanket Partition Load	0.00	kN/m²
Partition Load (U.N.O)	1.00	kN/m
	Timber Stud	

JetFloor Make Up

Beam	150mm	Jetfloor	White
Insulation	150mm	EPS Overlay	White
Topping	75mm	Structural Topping	
Bearing	FFL -	375	
U Value	0.127	W/m²k	

Jetfloor Block Key

Wide Block	W	485mm Beam Spacings
Narrow Block	N	295mm Beam Spacings
Cut Sheet	C	Tolerance Cut Sheet. No greater than 294mm

BISON PRECAST
a Forterra brand

Hoveringham Works, Thurgarton Lane, Hoveringham, Nottingham, NG14 7JX
TELEPHONE 01636 832000

This drawing and the copyright therein remain the property of Forterra

Housebuilder

miller homes

Site Address

Standard Drawings

Date	Scale	Drn.
31/10/24	1:50	JAE

Range

National Portfolio 2022

Type Description

L363 - Hampton

Rev A
